




CONSTRUCTION



Dover High School and Career Technical Center

Monthly Construction Report No. 13



October 3, 2017

TABLE OF CONTENTS

- A. Executive Summary
 - 1. Construction Documents Area Breakout Plan
 - 2. Construction Progress Highlights
 - 3. Critical Issues
 - 4. Summary

- B. Construction Status
 - 1. Schedule Building Phase Plan
 - 2. Monthly Construction Schedule Update
 - 3. 3-Week Look Ahead Schedule
 - 4. Schedule Impacts
 - 5. Progress Photos


- C. Design Coordination
 - 1. RFI's
 - 2. Submittals
 - 3. Architectural Supplemental Instructions

- D. Safety
 - 1. Safety Status

- E. Project Financial Status
 - 1. Procurement Update
 - 2. Current Contract Summary
 - 3. Change Order Management
 - 4. Contingency Usage
 - 5. Allowance Usage
 - 6. Billed to Date

A. Executive Summary:

1. Construction Documents Area Breakout Plan

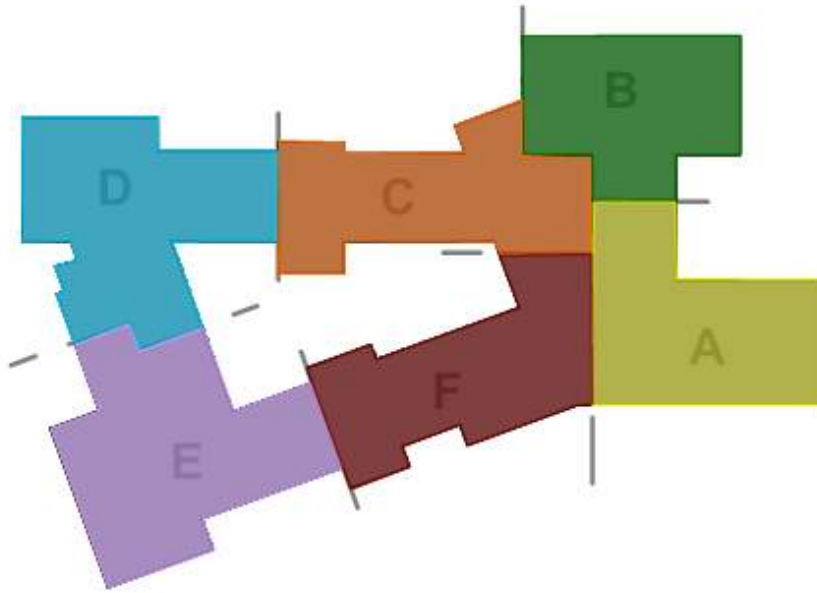

- ▶ Area A
 - Ground - Auditorium, Band, Food Service
 - First - Culinary Kitchen/Dining
 - Second - CTC Labs/Classrooms, Staff Dining
- ▶ Area B
 - Ground - Gymnasium, Alt PE, Locker Rooms
 - First - CTC Salon, Labs
 - Second - Life Sciences
- ▶ Area C
 - Ground - MEP, Weight Room, Team rooms, Marketing
 - First - Library, SPED, NJROTC, Offices, Guidance
 - Second - Business CR's, SPED CR's, Typical CR's
- ▶ Area D
 - Ground - N/A
 - First - Building Construction, Electrical, Wood Working, Typical CR's, Art
 - Second - Typical CR's, Sciences & Labs
- ▶ Area E
 - Ground - N/A
 - First - Typical CR's, Photography, Earth Science, Welding, Auto, CTE Offices/Admin
 - Second - Typical CR's, Sciences & Labs
- ▶ Area F
 - Ground - Town Square
 - First - SPED CR's, Pre-Engineering, Photo, Typical CR's, Admin, Nurse, Main Entry
 - Second - Computer, Typical CR's

2. Construction Progress Highlights

- Interior drywall in Areas A & B is nearly complete
- Interior framing in Areas D & F are complete
- Interior drywall in Area C is on-going
- Window and Curtainwall installation has begun
- RTU placement has begun
- Interior piping, ductwork and electrical are on-going
- Interior concrete slab placement is substantially complete

3. Critical Issues

- Finalization and issuance of color selections so materials can be ordered and delivered for installation. Resolution of recent code questions from Inspectional Services.


4. Summary

- The project is currently proceeding smoothly. Safety has been good to date.

B. Construction Status:

1. Schedule Phase Plan

- For scheduling purposes, the building is separated into three areas – Building 1, Building 2 and Building 3. These are defined as separate areas separated by a fire rated expansion joint.

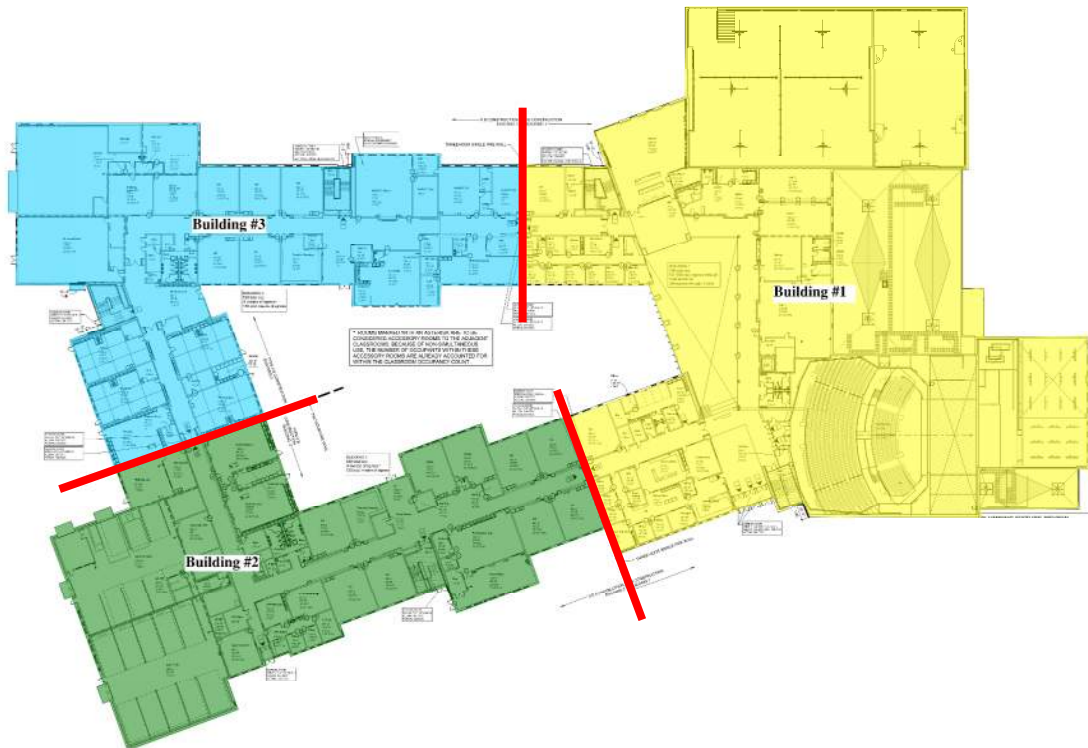

2. Monthly Schedule Update – 9/29/17 update provided.

3. Three-Week Look Ahead Schedule – Distributed weekly

4. Schedule Impacts

- Analyzing impact due to volume of changes to documents.


5. Progress Photos

- Auditorium Concrete Steps Complete



Dover HS & CTC - Monthly Report for September, 2017

- Town Square Curtainwall Installation

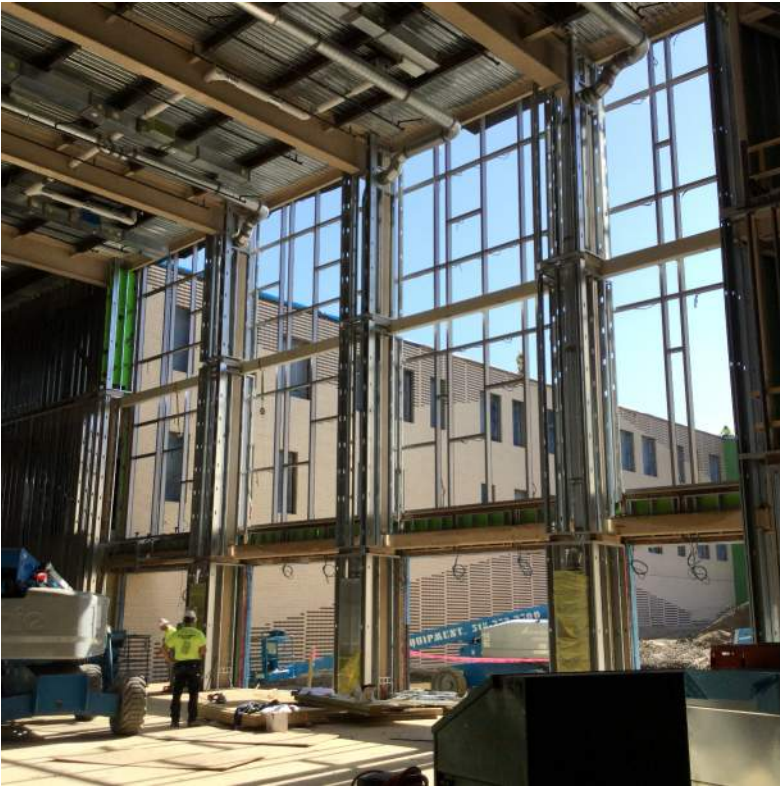

- Courtyard Seatwall Foundations



Dover HS & CTC - Monthly Report for September, 2017

- South Elevation @ CTC Entrance



- Library Elevation



- RTU Installation Area A



C. Design Coordination:

1. RFI Status
 - Submitted (561)
 - Open (08)
 - Critical (01)
2. Submittals
 - Submitted (760)
 - Open (21)
 - Critical (00)
3. ASI's & PR's
 - Issued (137)

D. Safety Update:

1. PC has a site specific safety program in place for this project. Every worker who comes on site is required to be oriented to the project rules and expectations. Safety has been good to date.

PC's on-site safety specialist does a weekly audit and provide the team with a safety score from 0 to 100. Below are the most recent scores.

Week of 9/05/17 = 82

Dover HS & CTC - Monthly Report for September, 2017

Week of 9/12/17 = 84

Week of 9/19/17 = 85

Week of 9/26/17 = 65

E. Project Financial Status:

1. Procurement Update: Letters of Recommendation (LOR's) Issued and Signed

• 02.01 Demolition & Asbestos Abatement	\$ 2,193,895
• 03.01A Concrete Foundations	\$ 1,800,000
• 03.01B Concrete Flatwork	\$ 2,019,559
• 04.01 Masonry	\$ 3,450,000
• 05.01 Structural Steel	\$ 6,400,000
• 05.02 Miscellaneous Metals	\$ 755,350
• 06.01A Architectural Millwork	\$ 409,199
• 06.01B Laboratory Equipment	\$ 159,090
• 06.01C Laboratory Casework	\$ 989,575
• 07.01 Below Grade Waterproofing	\$ 41,600
• 07.01 Air & Vapor Barrier	\$ 445,770
• 07.02 Roofing and Flashing	\$ 1,770,000
• 07.03 Applied Fireproofing	\$ 328,320
• 07.05 Firestopping	\$ 54,750
• 08.01 Doors, Frames & Hardware	\$ 570,897
• 08.02 Windows, Storefront & Curtainwall	\$ 2,935,827
• 08.03 Overhead Doors	\$ 64,000
• 09.01 Metal Stud Framing & Drywall	\$ 5,550,000
• 09.02 Acoustical Ceilings	\$ 574,473
• 09.02 Acoustical Wall Panels	\$ 371,000
• 09.03 Ceramic Tile	\$ 640,000
• 09.03 Resilient Flooring	\$ 953,000
• 09.04 Stage and Gymnasium Flooring	\$ 159,000
• 09.05 Resilient Athletic Flooring	\$ 49,000
• 09.06 Painting	\$ 600,000
• 10.01 Miscellaneous Accessories	\$ 601,678
• 11.01 Kitchen Equipment	\$ 467,822
• 11.03 Stage Rigging & Curtains	\$ 320,000
• 11.04 Athletic Equipment	\$ 132,400
• 12.01 Window Treatments	\$ 76,700
• 12.02 Gymnasium and Auditorium Seating	\$ 261,823
• 14.01 Elevators	\$ 211,131
• 21.01 Fire Protection	\$ 540,000
• 23.01 Plumbing	\$ 2,490,000
• 23.01 Ductwork	\$ 2,645,270
• 23.01 Mechanical	\$ 2,241,750
• 23.01 Testing & Balancing	\$ 77,300
• 23.02 Automatic Temperature Controls	\$ 761,465

Dover HS & CTC - Monthly Report for September, 2017

• 23.04 Condensing Boilers	\$ 99,108
• 23.05 Air Handling Equipment & Chiller	\$ 1,690,000
• 26.01 Electrical, Telecom & Security	\$ 6,784,800
• 31.01 Sitework	\$ 4,546,082
• 31.02 Rammed Aggregate Piers	\$ 285,917
• 31.03 Turf Field	\$ 417,250
• 32.02 Fencing	\$ 128,881
• 03.2A Courtyard Concrete	\$ 241,600
• 32.1A Courtyard Landscaping	\$ 85,020
• 32.1B Courtyard Hardscaping	\$ 127,110

○ Total to Date \$55,696,592

2. Current Contract Summary

• Base Contract:	\$71,643,000
• Approved Changes thru CO #8	\$ 910,414
• Current Contract amount:	\$72,553,414

3. Change Order Management:

Previously Approved Proposals	\$ 910,414
Proposals to be included in CO No. 9:	
• 190020.2	\$ 189,382
• 190058	(\$ 152)
• 190060R1	\$ 22,776
• 190065	\$ 18,387
• 190089R2	\$ 5,080
• 190103R1	\$ 7,485
• 190115	(\$ 5,238)
• 190124	(\$ 337)
• 190128	\$ 498
• 190137	\$ 609
• 190148	(\$ 4,256)

• Total \$ 1,144,648

4. Contingency Usage

• Carried:	\$ 1,700,000
• Committed to Date:	\$ 1,123,760
• Remaining:	\$ 576,240

5. Allowance Status

	<u>Used</u>	<u>Remaining</u>
• Hazardous Abatement	\$ 2,241	\$ 1,089,759
• Animal Science Building	\$36,358	\$ 1,163,642
• Climbing Wall	\$0	\$ 35,000

Dover HS & CTC - Monthly Report for September, 2017

6. Application for Payment Status

• Requisitioned to Date Thru #16 (Draft)	\$39,063,177
• Current Retained Amount	\$ 1,595,032
• Remaining to be Billed	\$35,085,270
