




Henry Law Avenue and Payne Street Reconstruction Project

JULY 23, 2026 PUBLIC INFORMATIONAL MEETING




Community Services
Dover, NH


Meeting Agenda

- Introductions
- Project Boundary
- Project Objective
- Construction Phasing
- Traffic and Parking Impacts
- Schedule
- Questions and Answers

Project Boundary- Phase 1&2

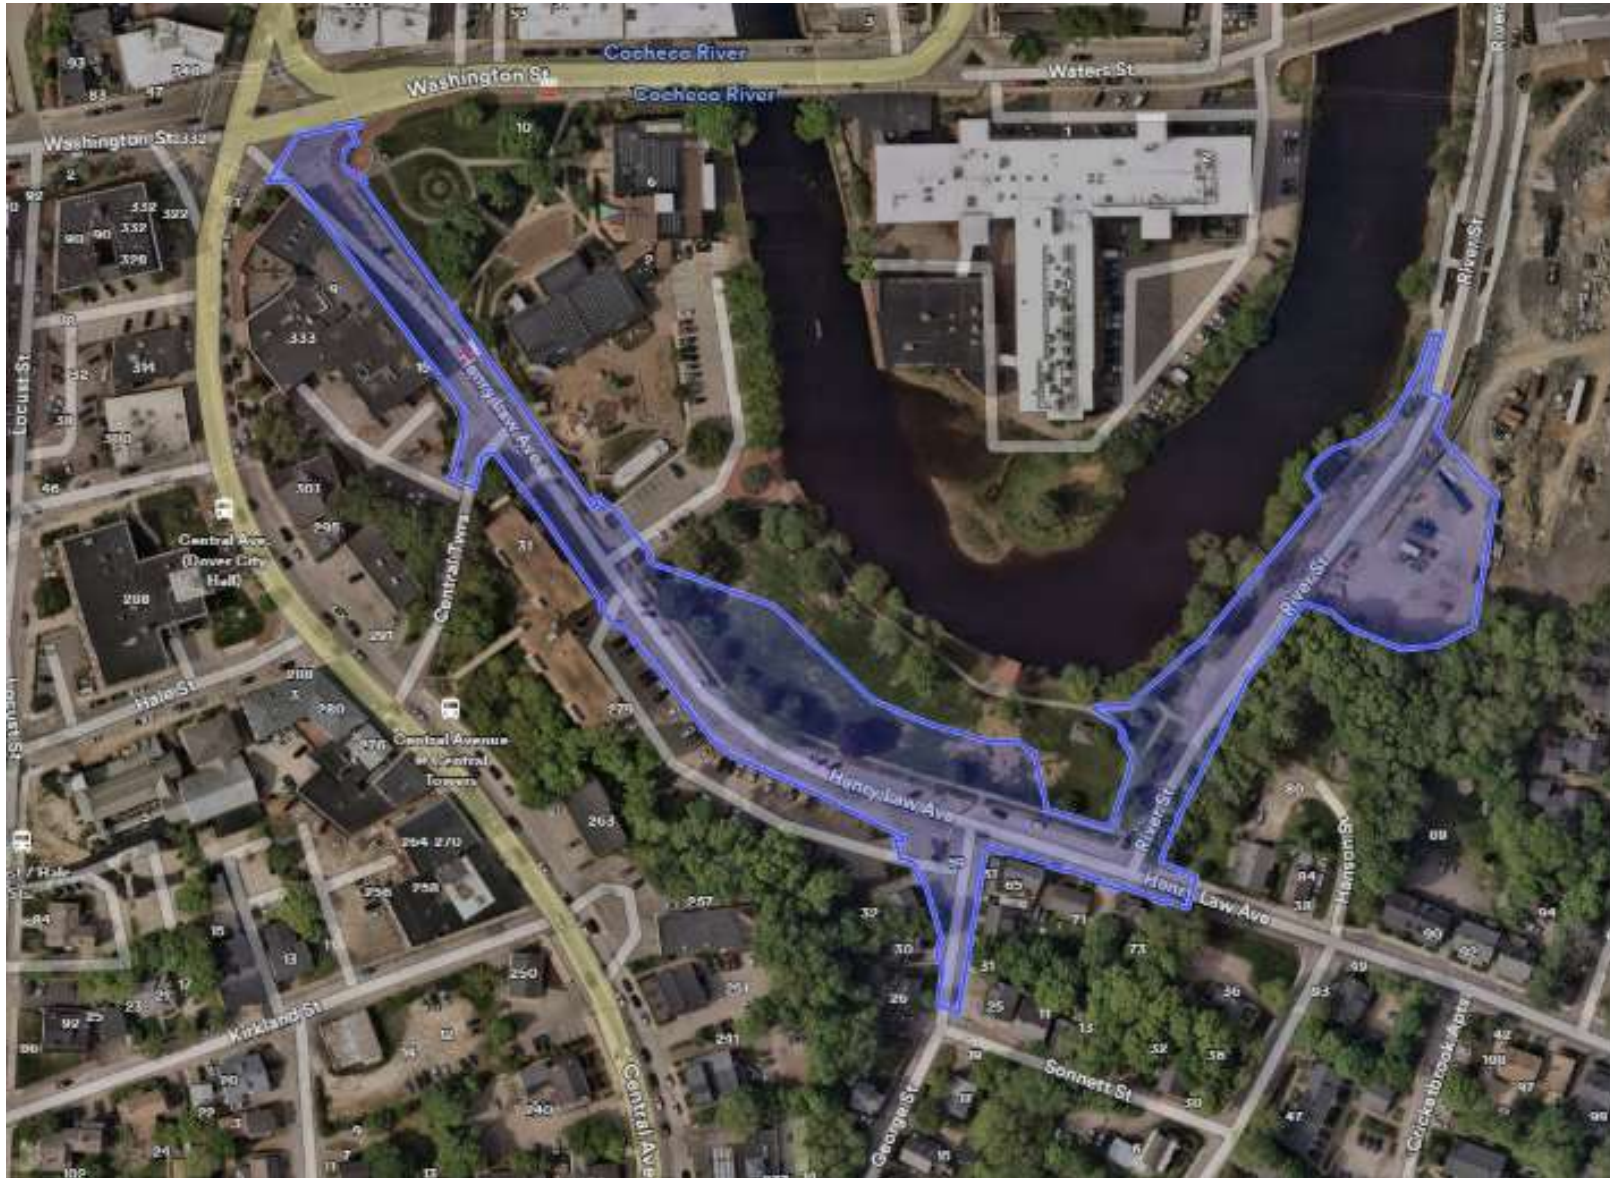

Project Boundary- Phase 3

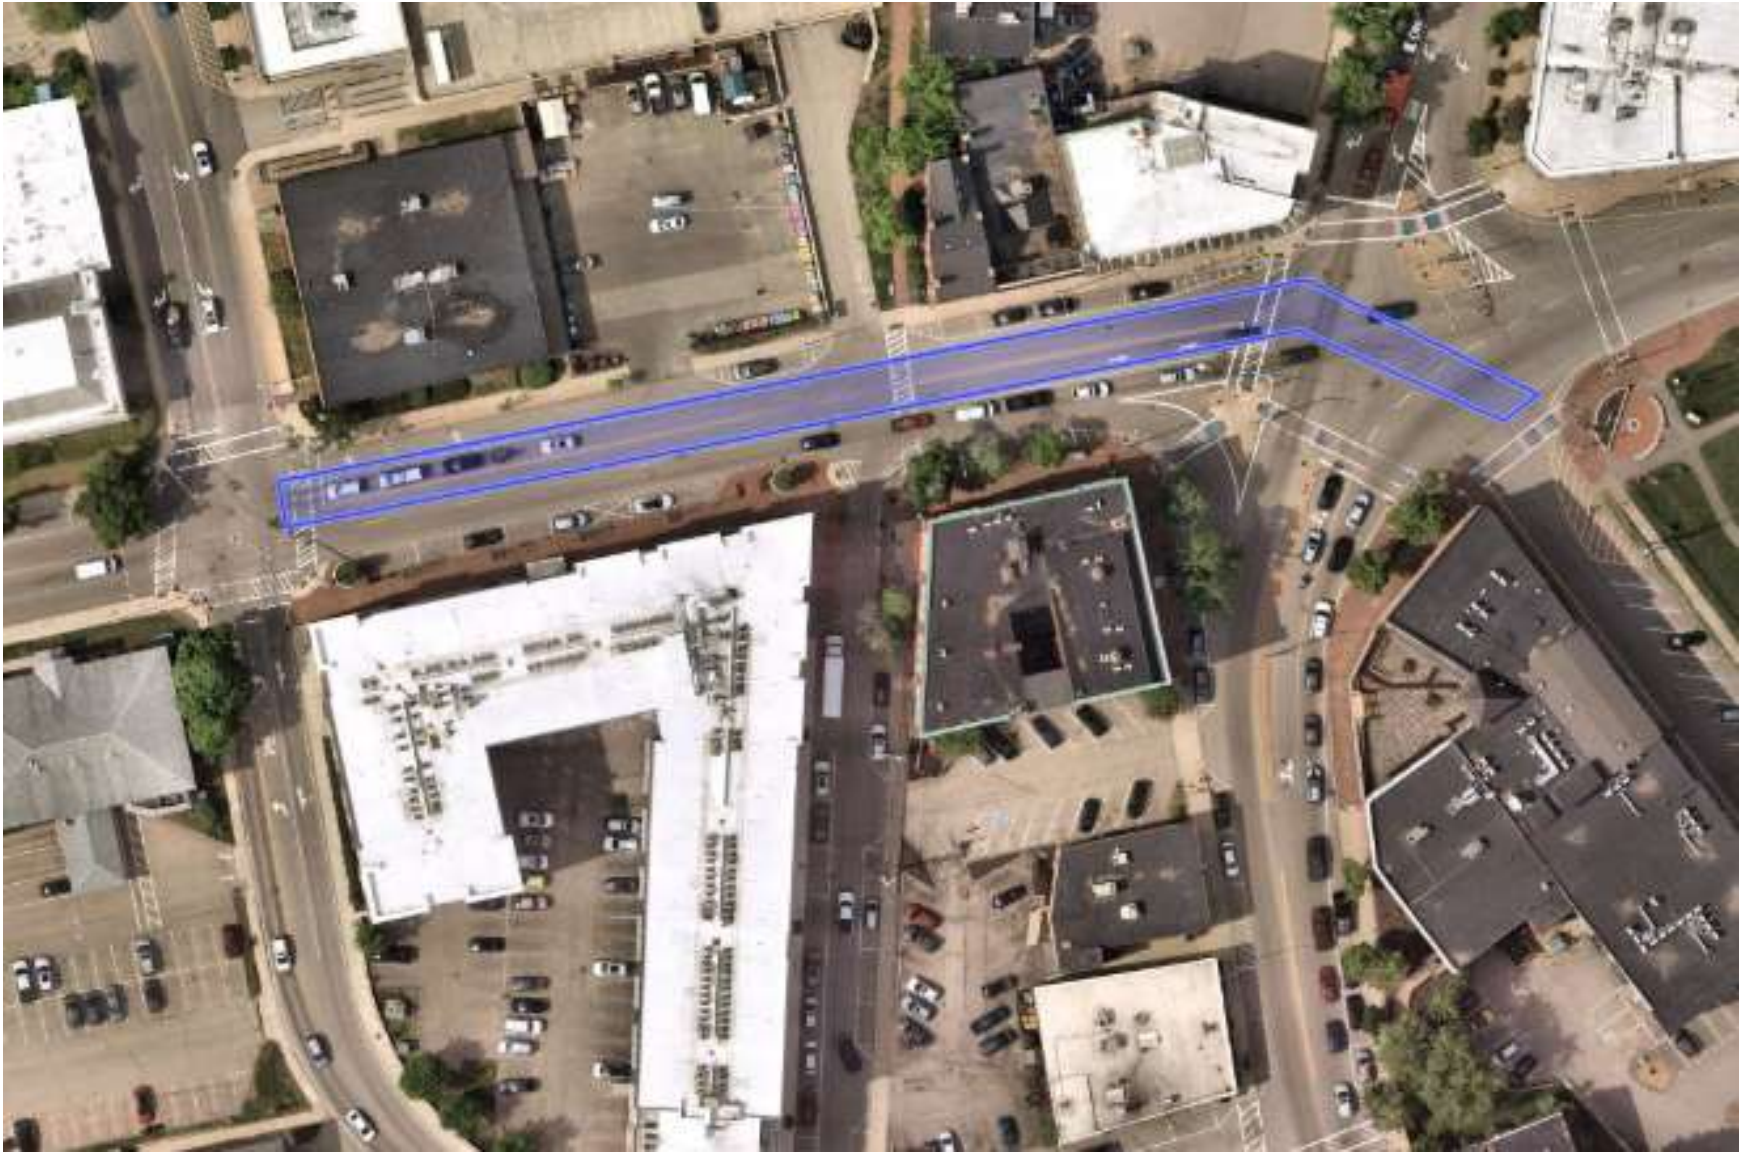

Project Objectives

Utility Upgrades

■ Sewer

- Main Trunk Line Replacement
- CIPP Lining on Payne Street

■ Stormwater

- New Drainage Mains and Structures Throughout
- Upgrades to Two Major Outfalls
- Two Subsurface Soil Filtration Systems

■ Water


- Replace Aging Cast Iron Main on George St
- New Hydrants

■ Electrical

- Relocation of all Overhead Power Lines to Belowground
- Stage and Pavilion Power, Ornamental Lighting

Project Objectives

BMP-100 Soil Filtration System

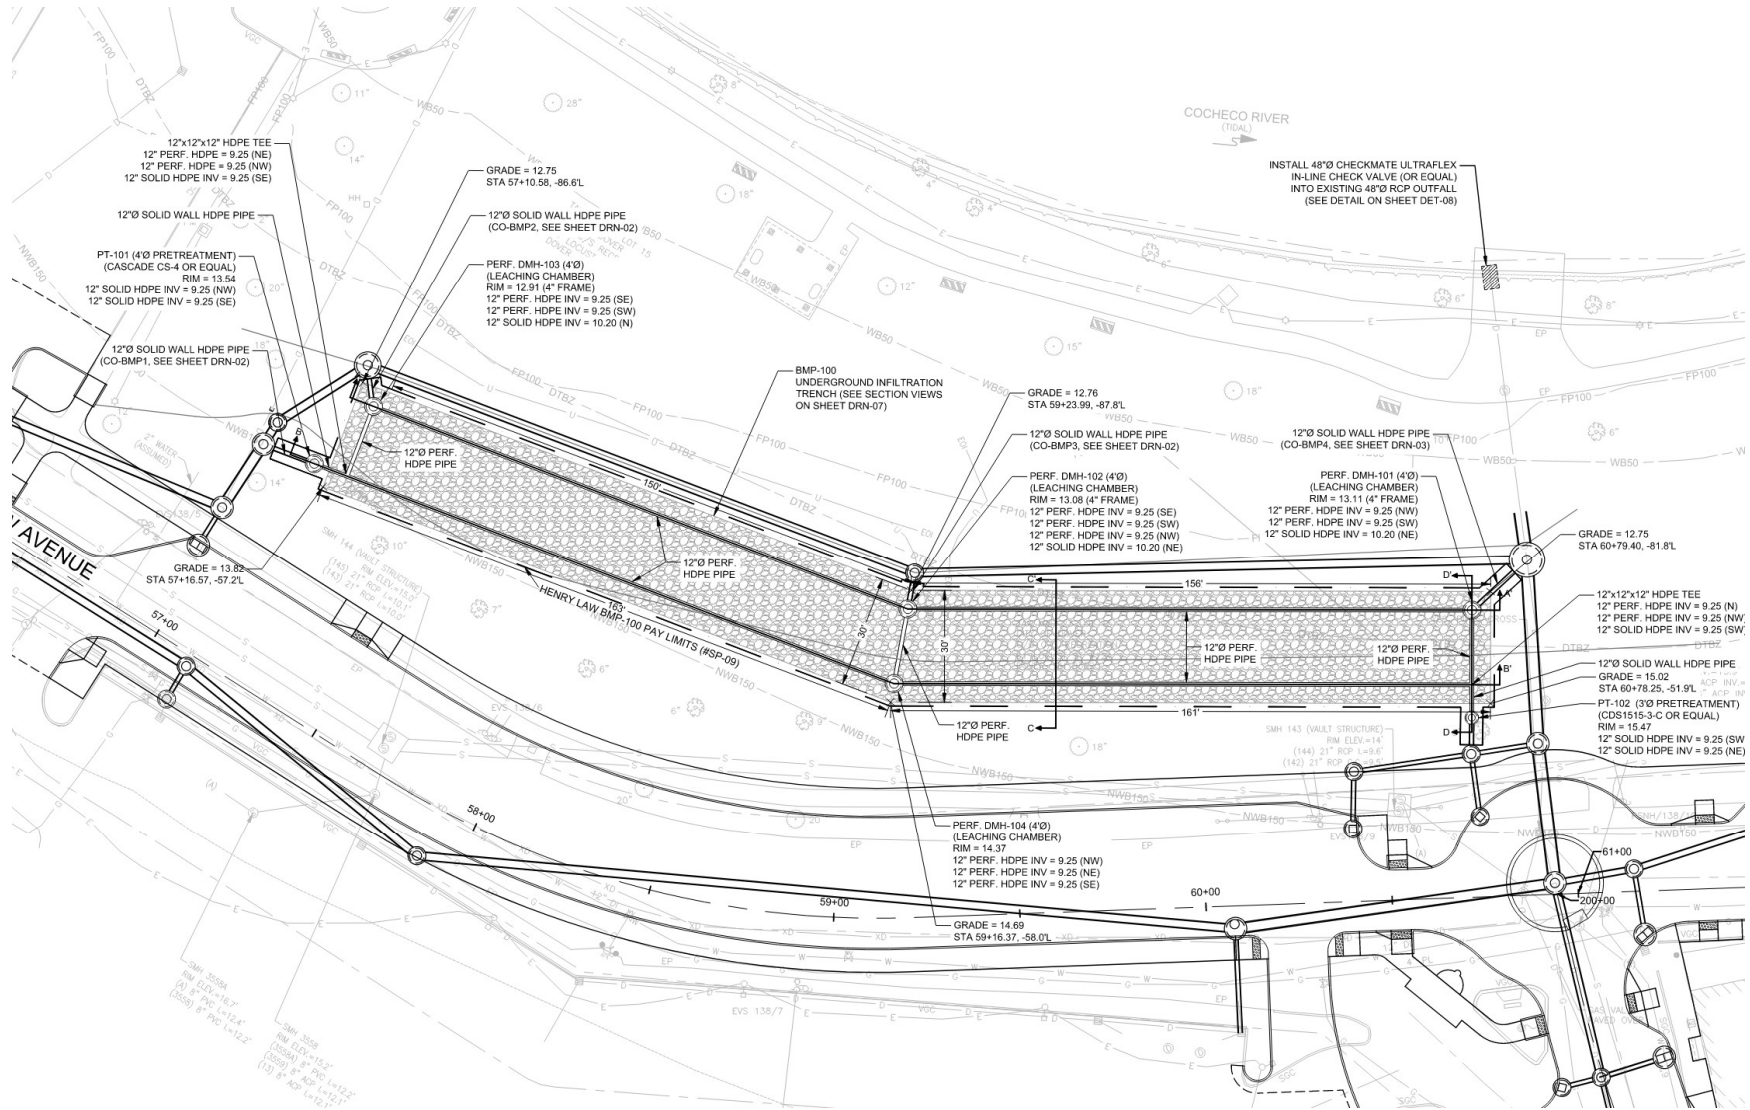

[illegible]

Project Objectives

Utility Upgrades

■ Sewer

- Main Trunk Line Replacement
- CIPP Lining on Payne Street

■ Stormwater

- New Drainage Mains and Structures Throughout
- Upgrades to Two Major Outfalls
- Two Subsurface Soil Filtration Systems

■ Water

- Replace Aging Cast Iron Main on George St
- New Hydrants


■ Electrical

- Relocation of all Overhead Power Lines to Belowground
- Stage and Pavilion Power, Ornamental Lighting

Project Objectives

Roadway Reconstruction


- Complete Roadway Reconstruction, Sidewalks and Crosswalks
- George Street Roundabout

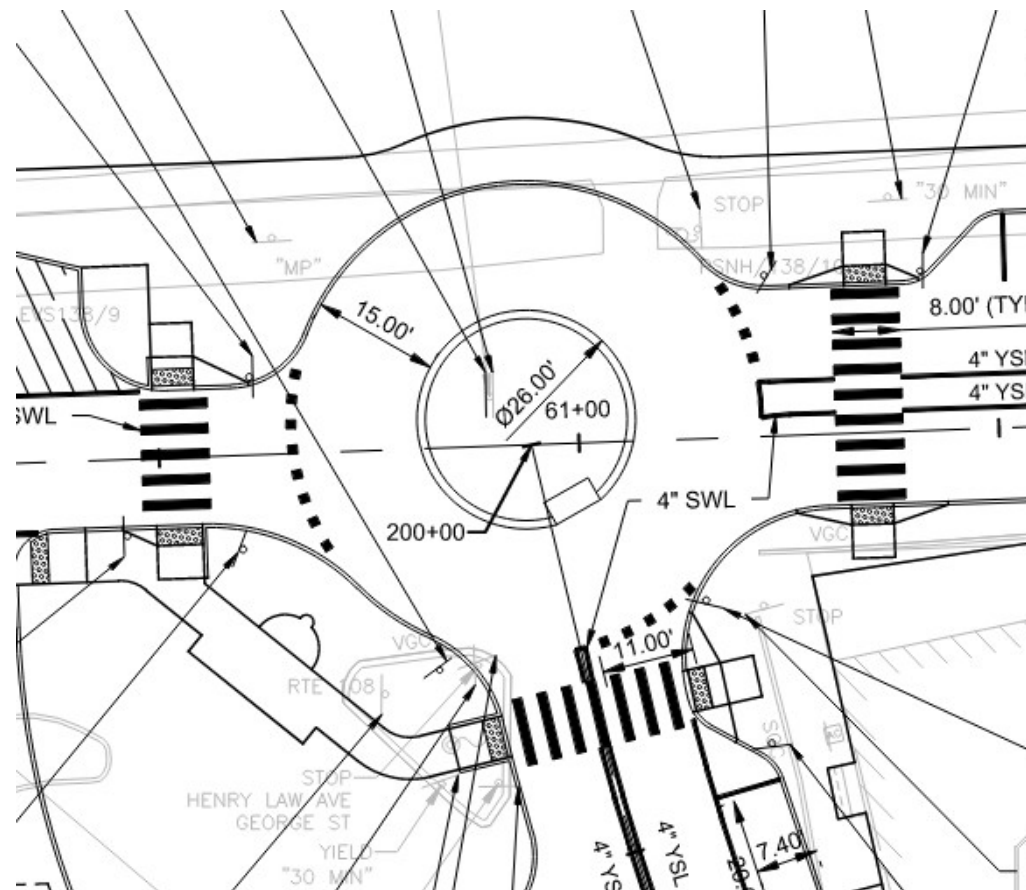

Project Objectives


Roadway Reconstruction

- New Payne St. Parking Lot

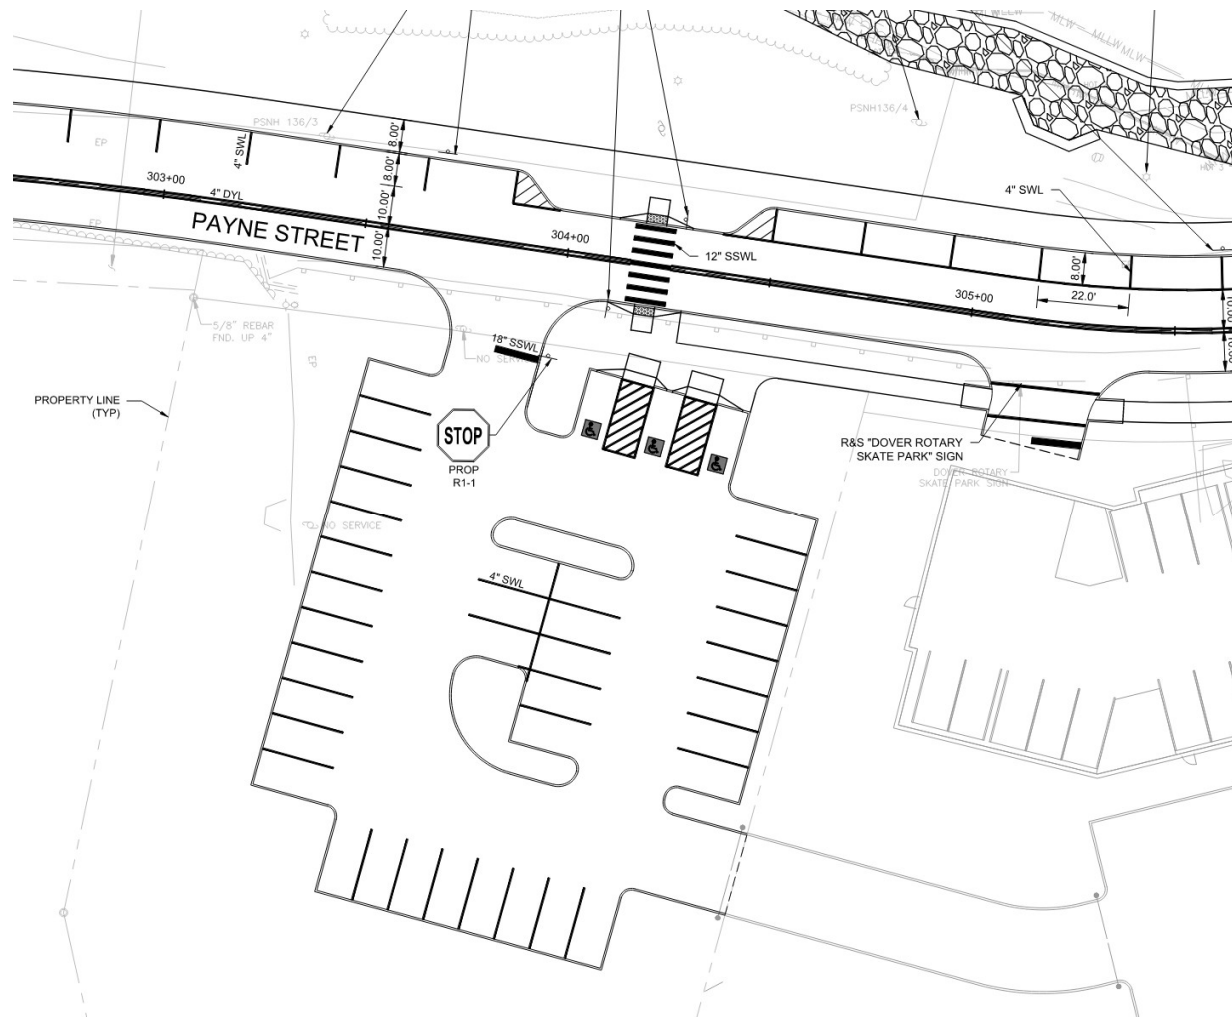





Phase 1

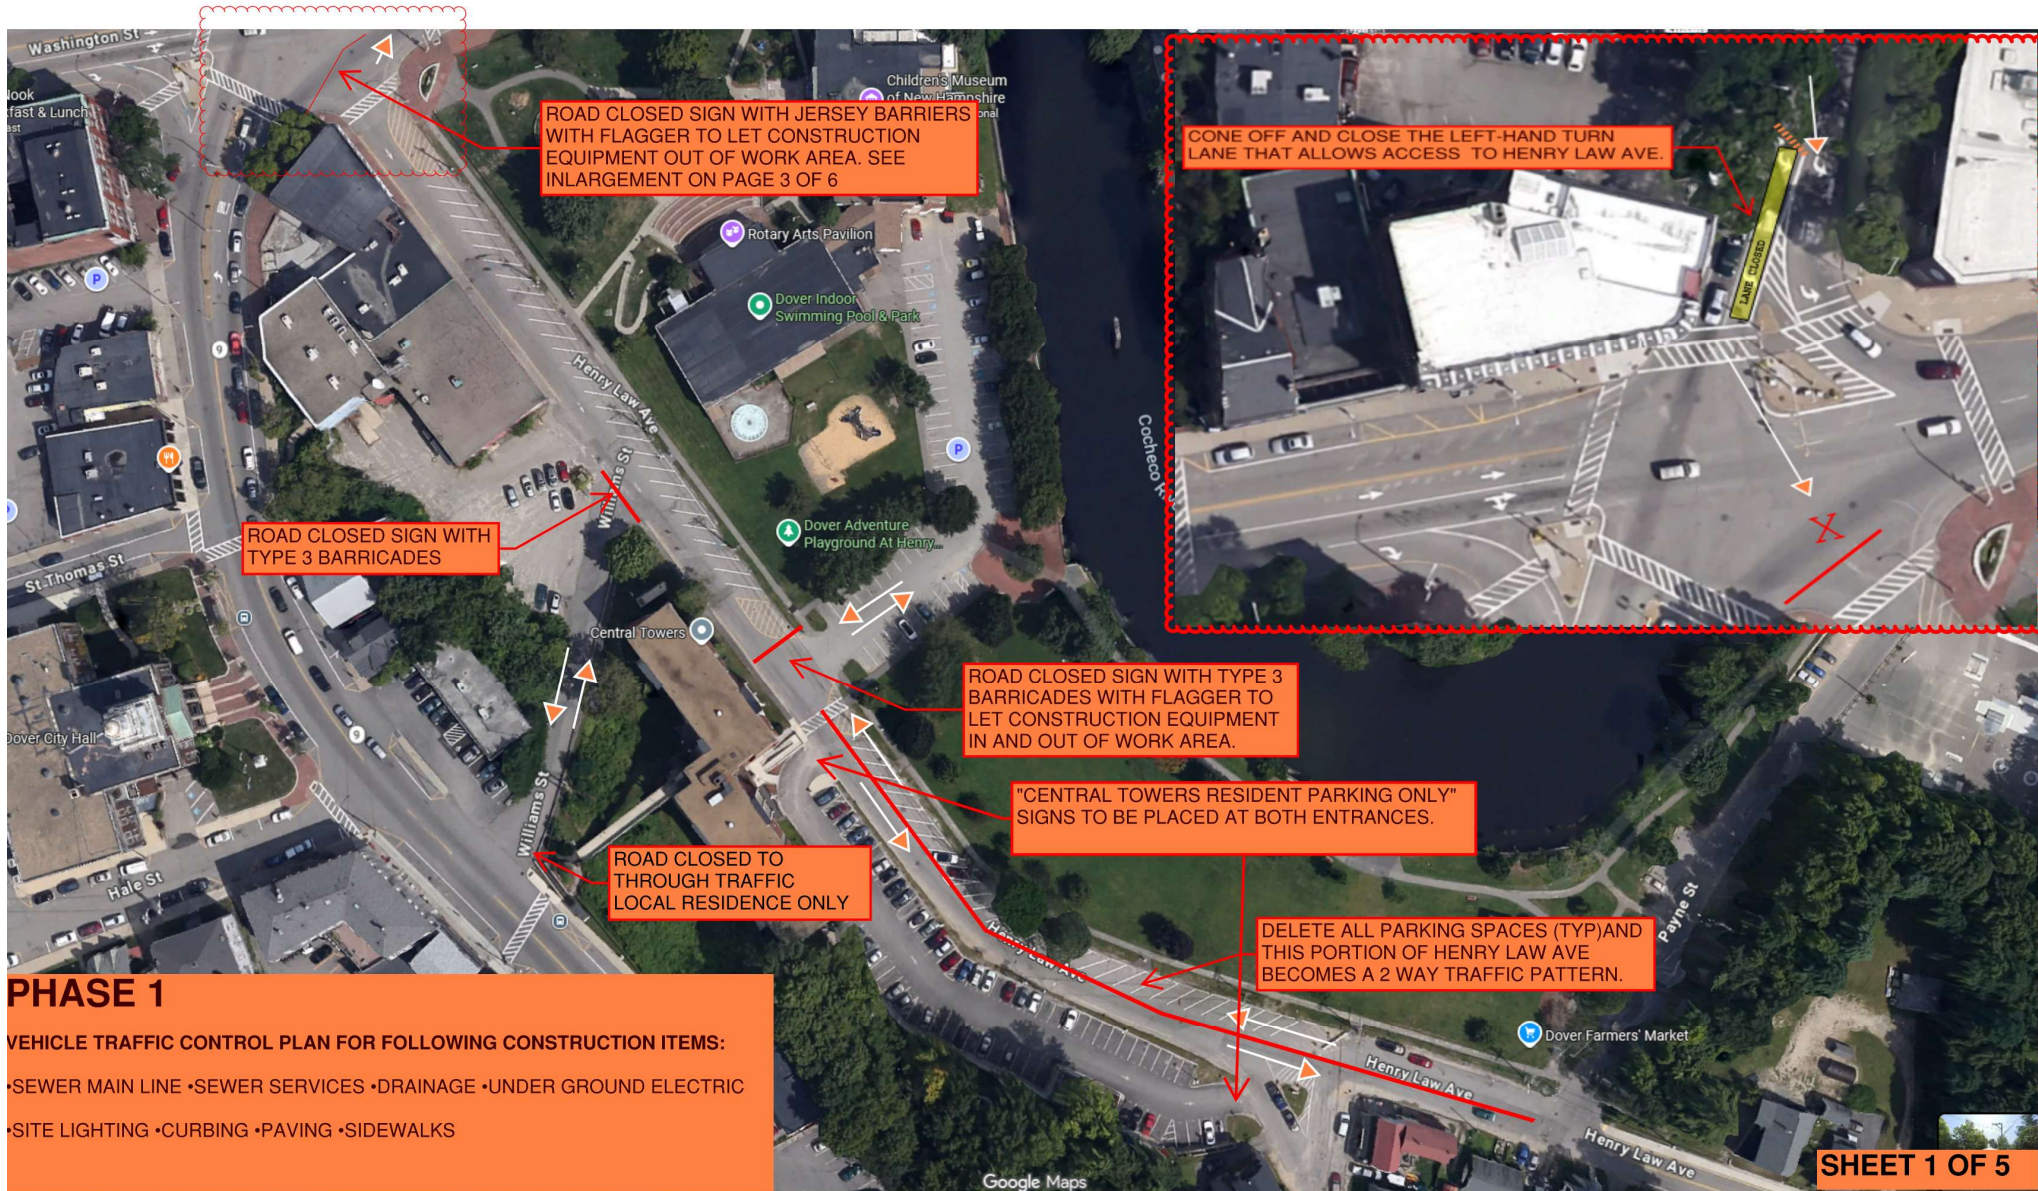


Phase 1

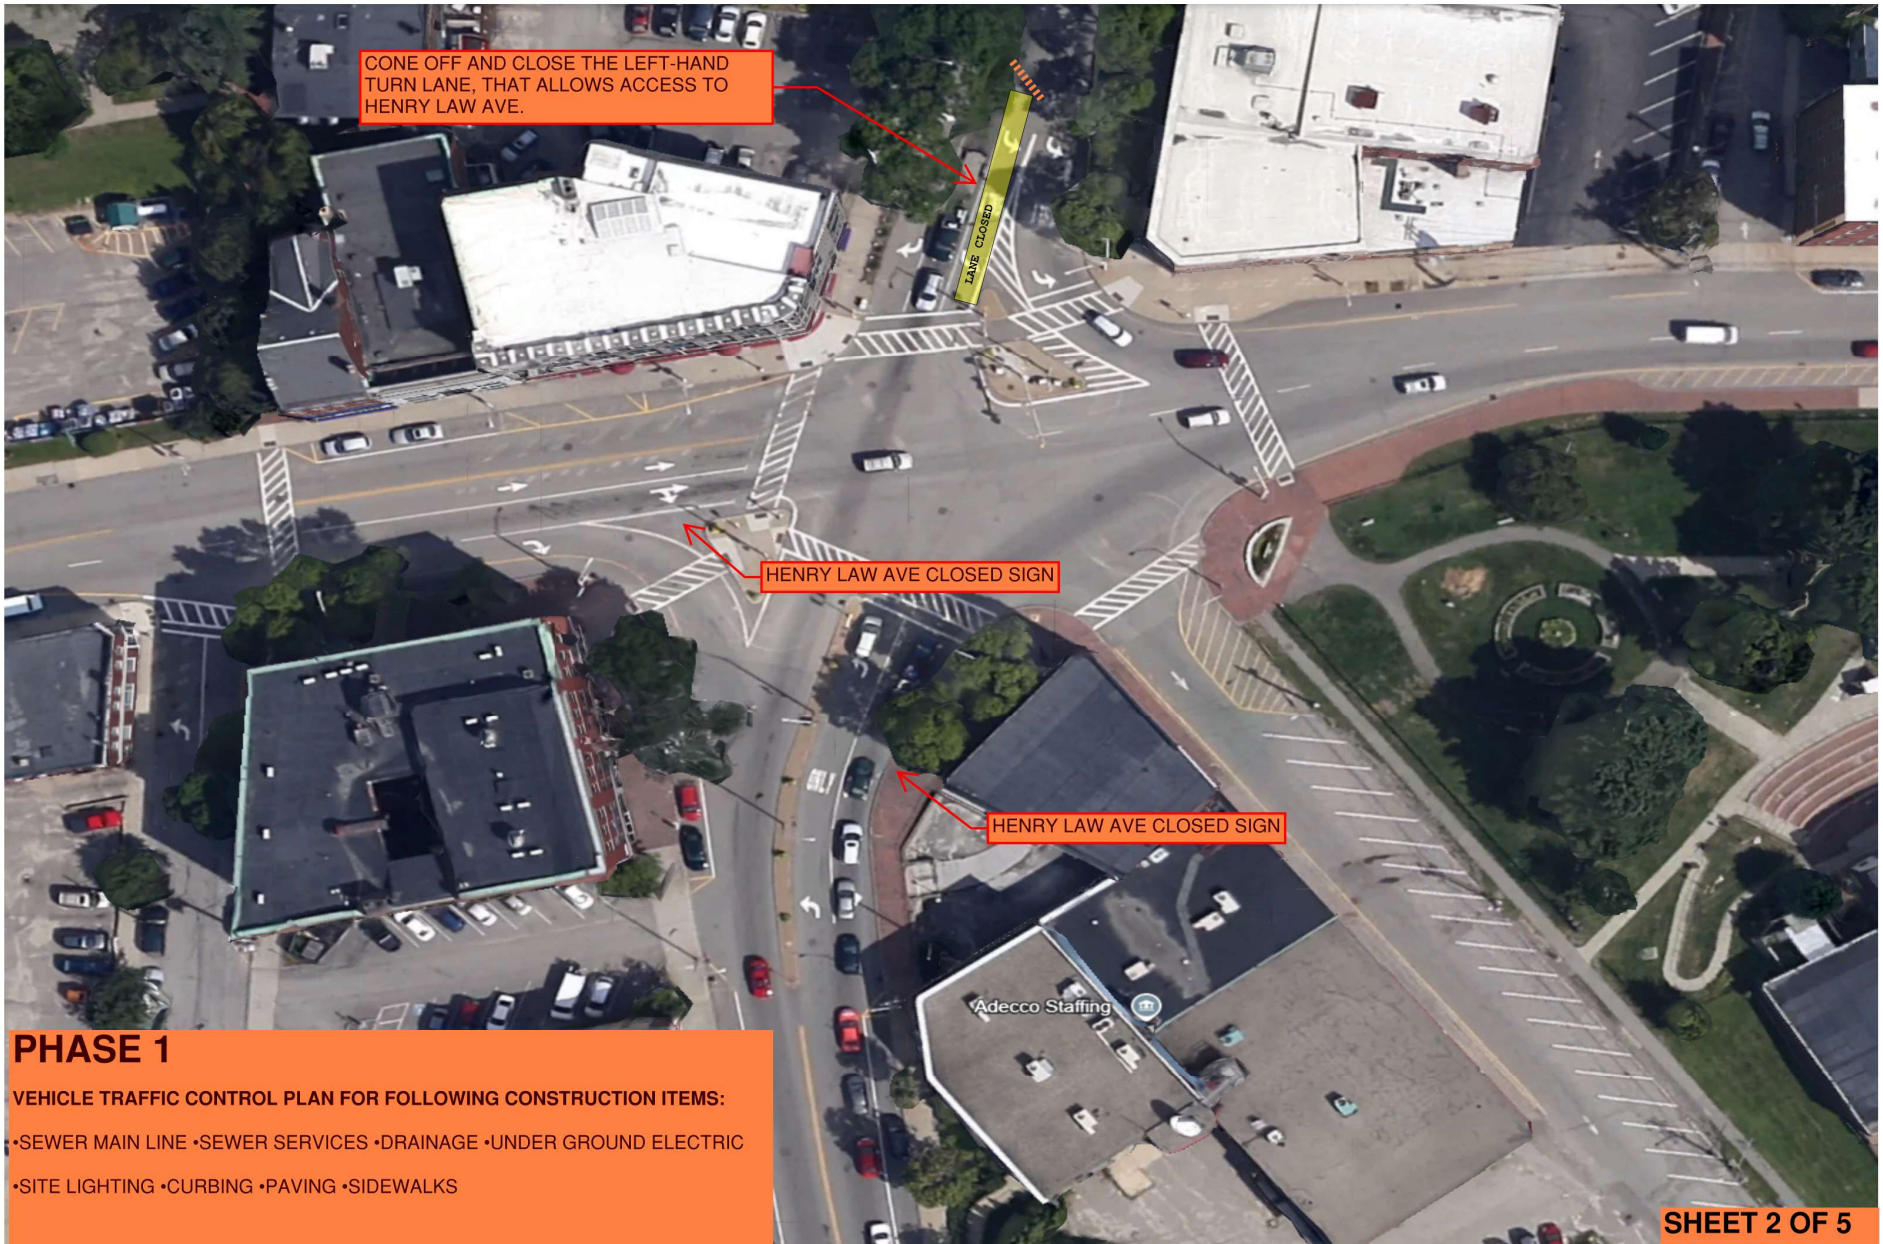

Phase 1

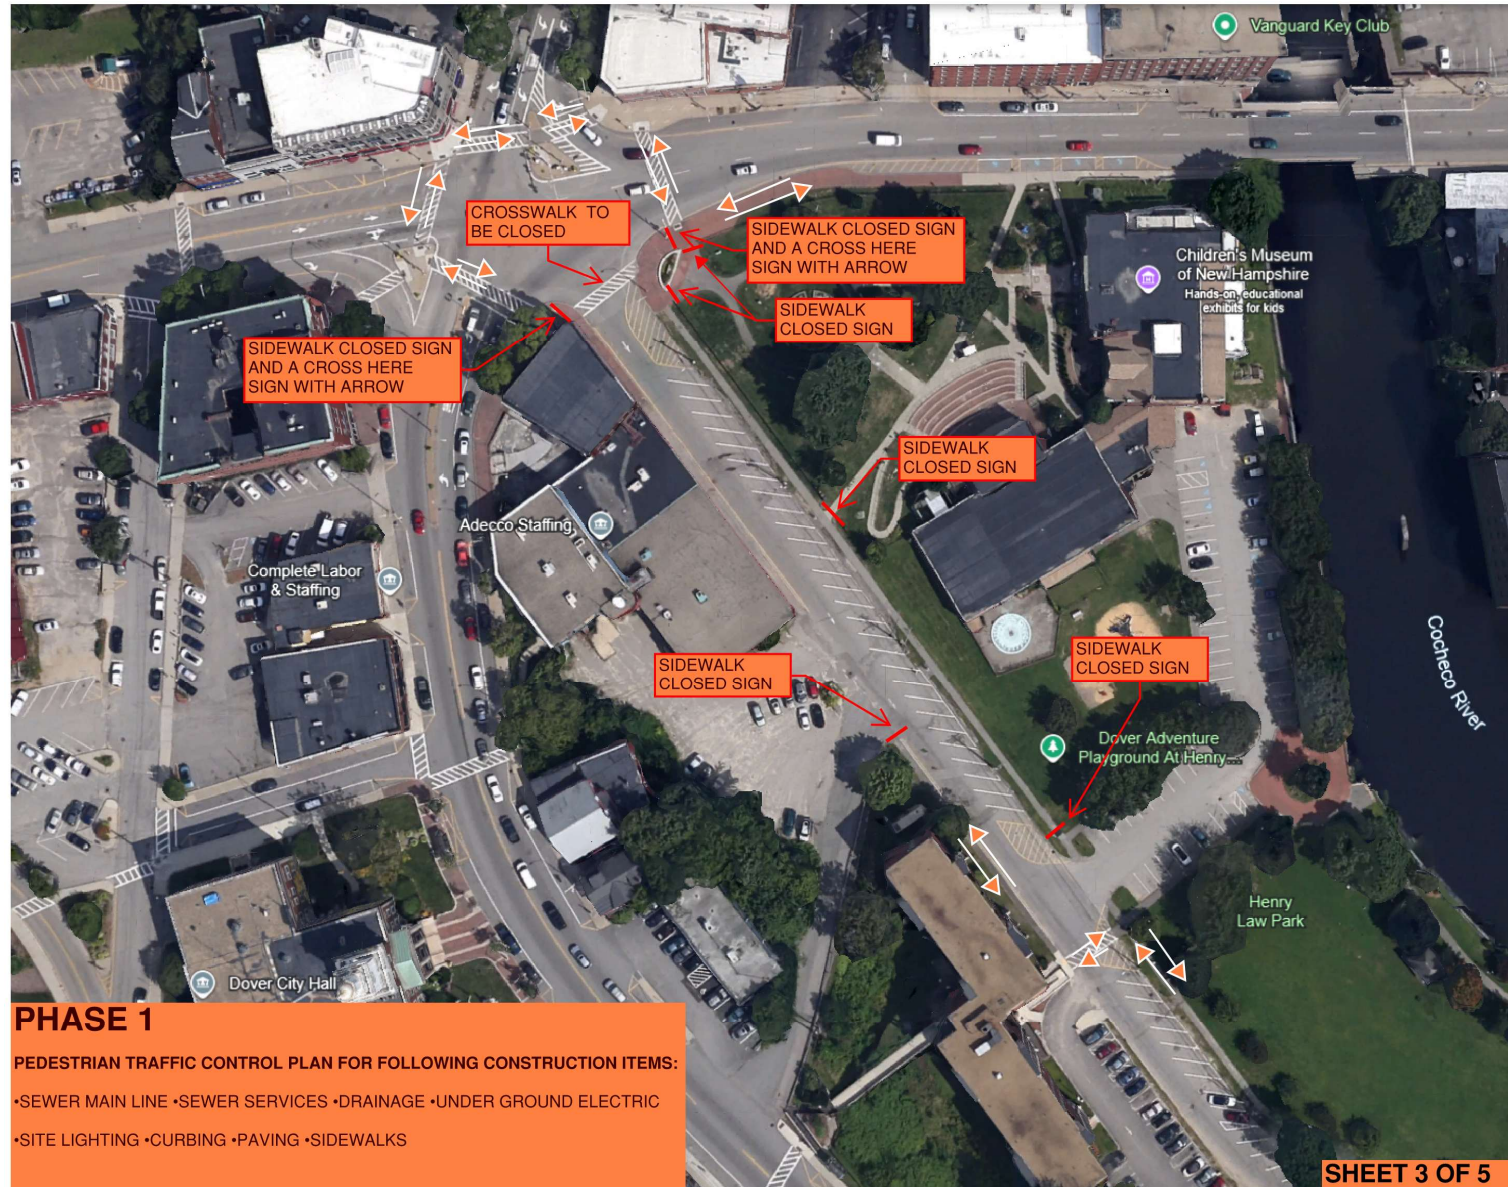


Phase 1

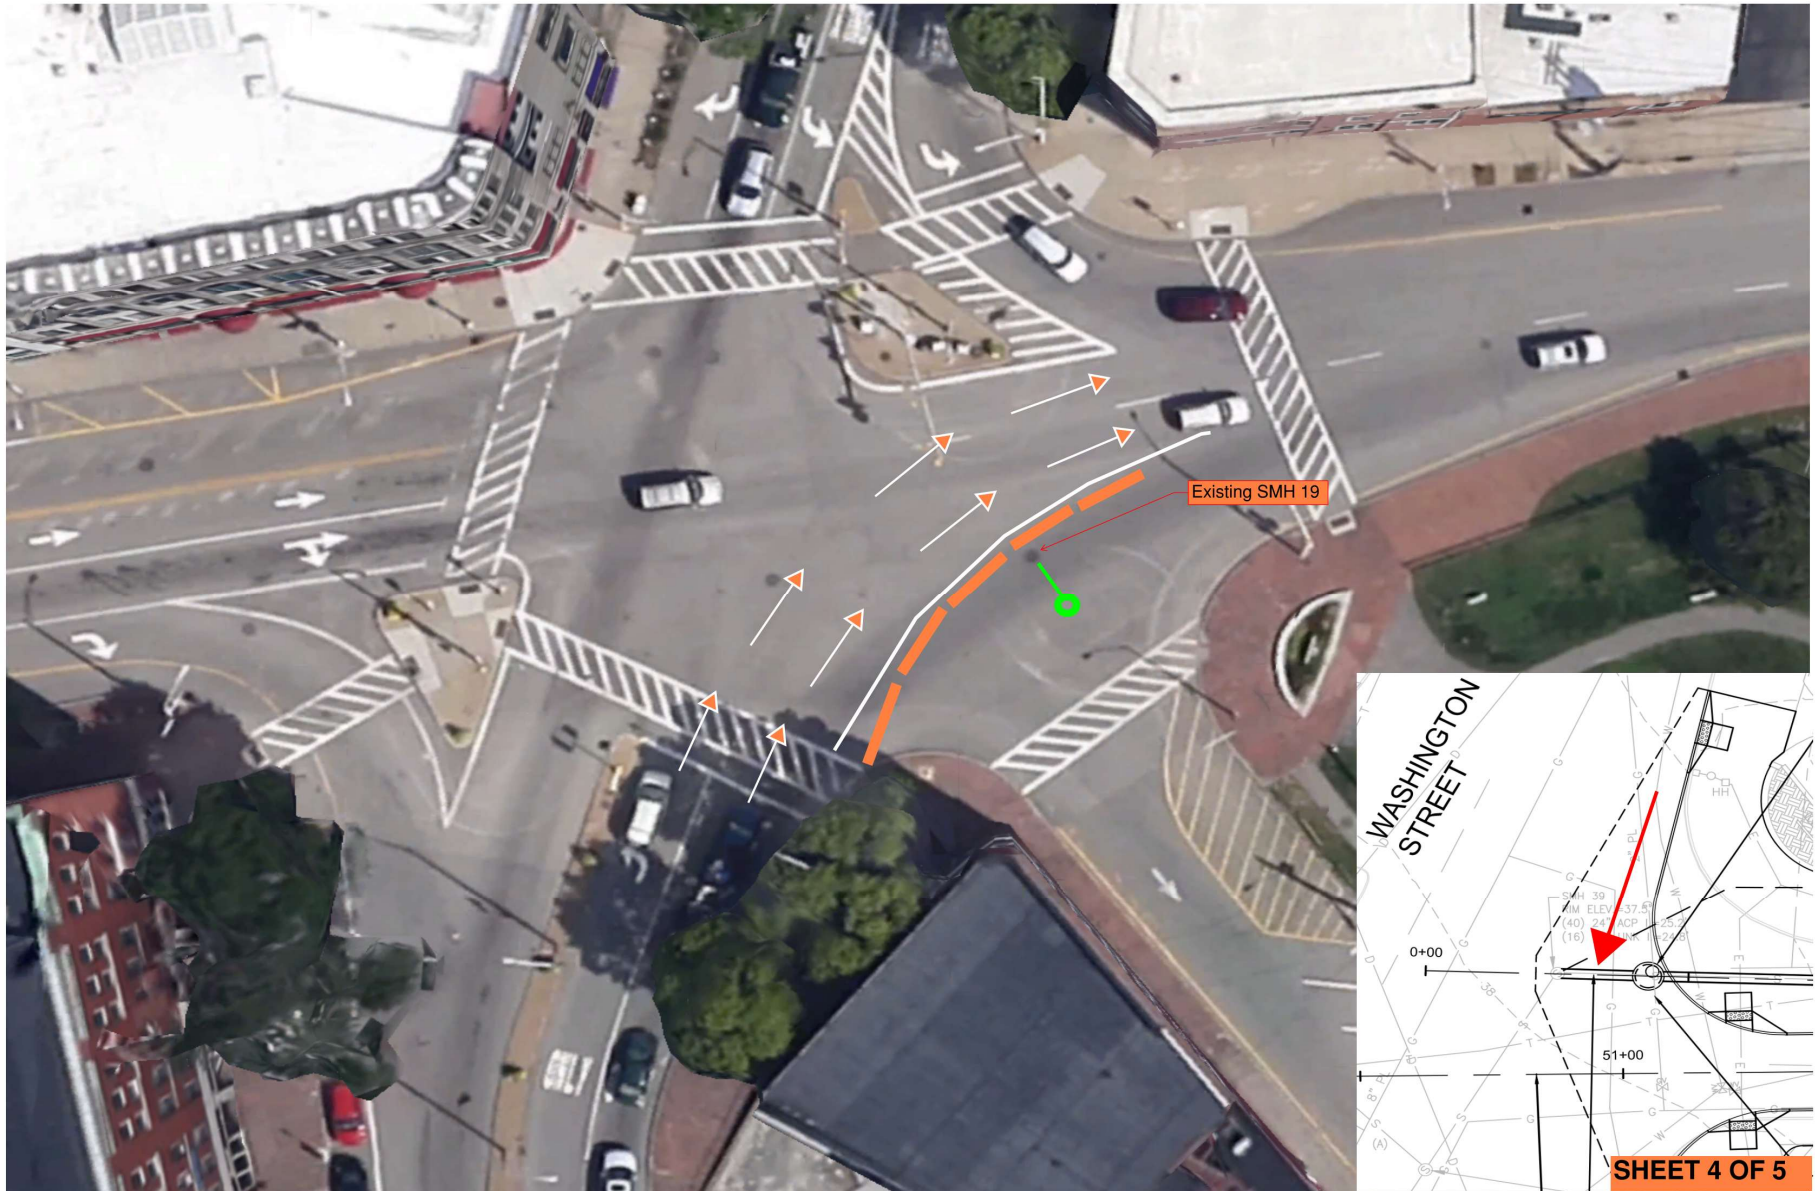


Community Services
Dover, NH



Phase 2

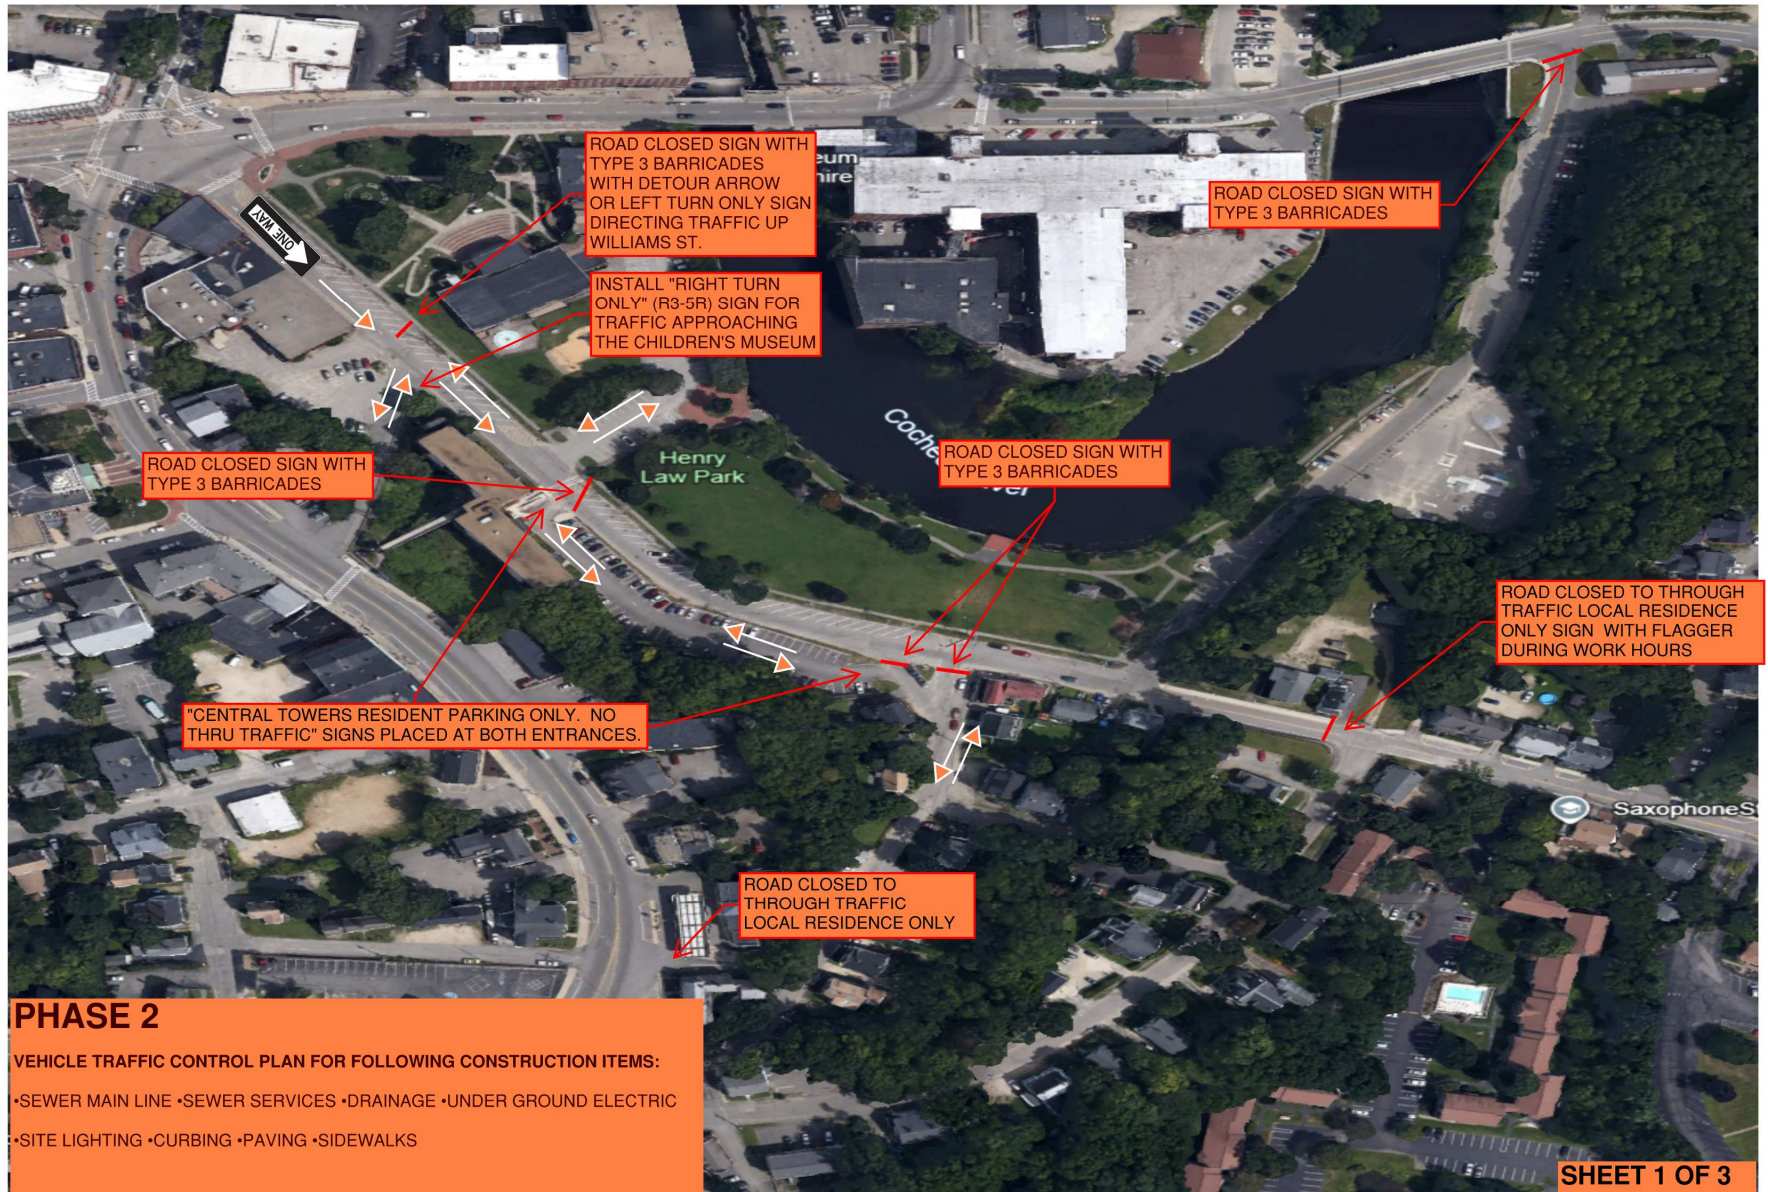


Phase 2

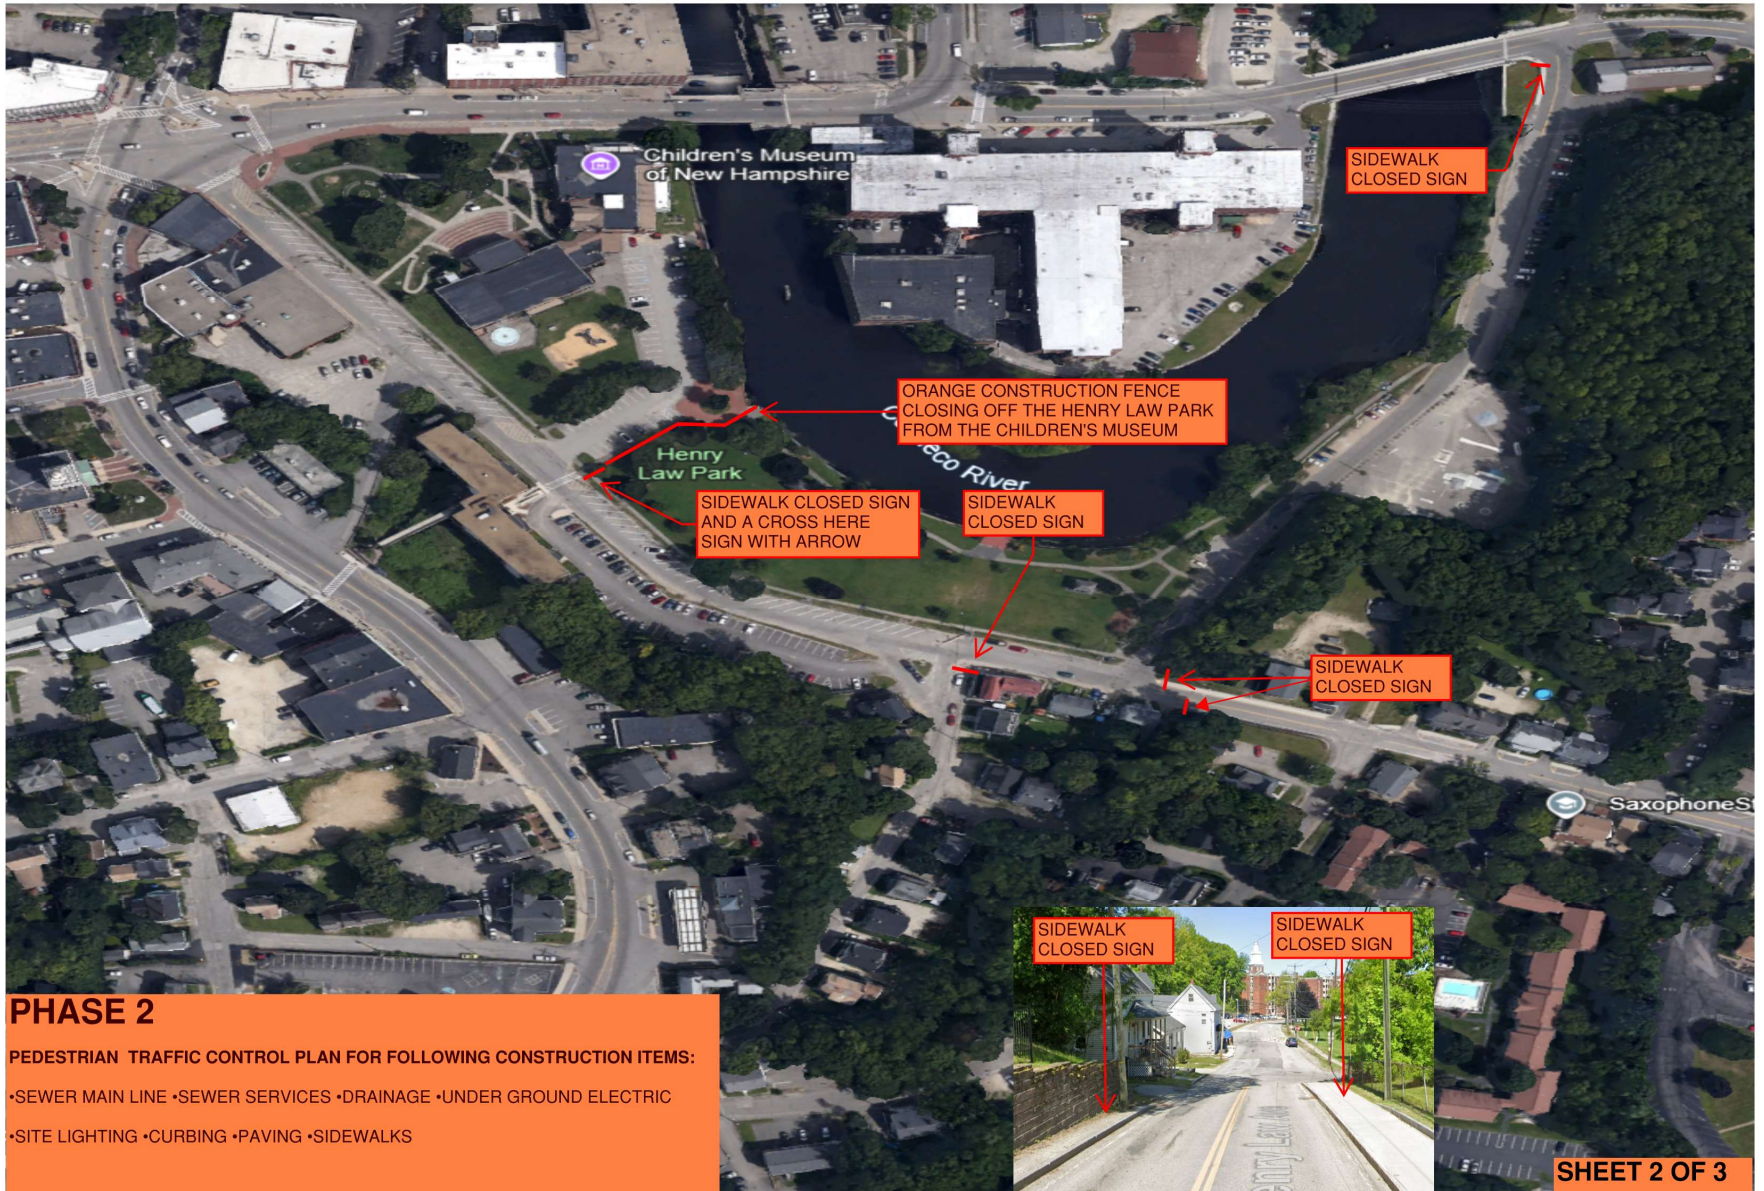


Phase 2



Community Services
Dover, NH

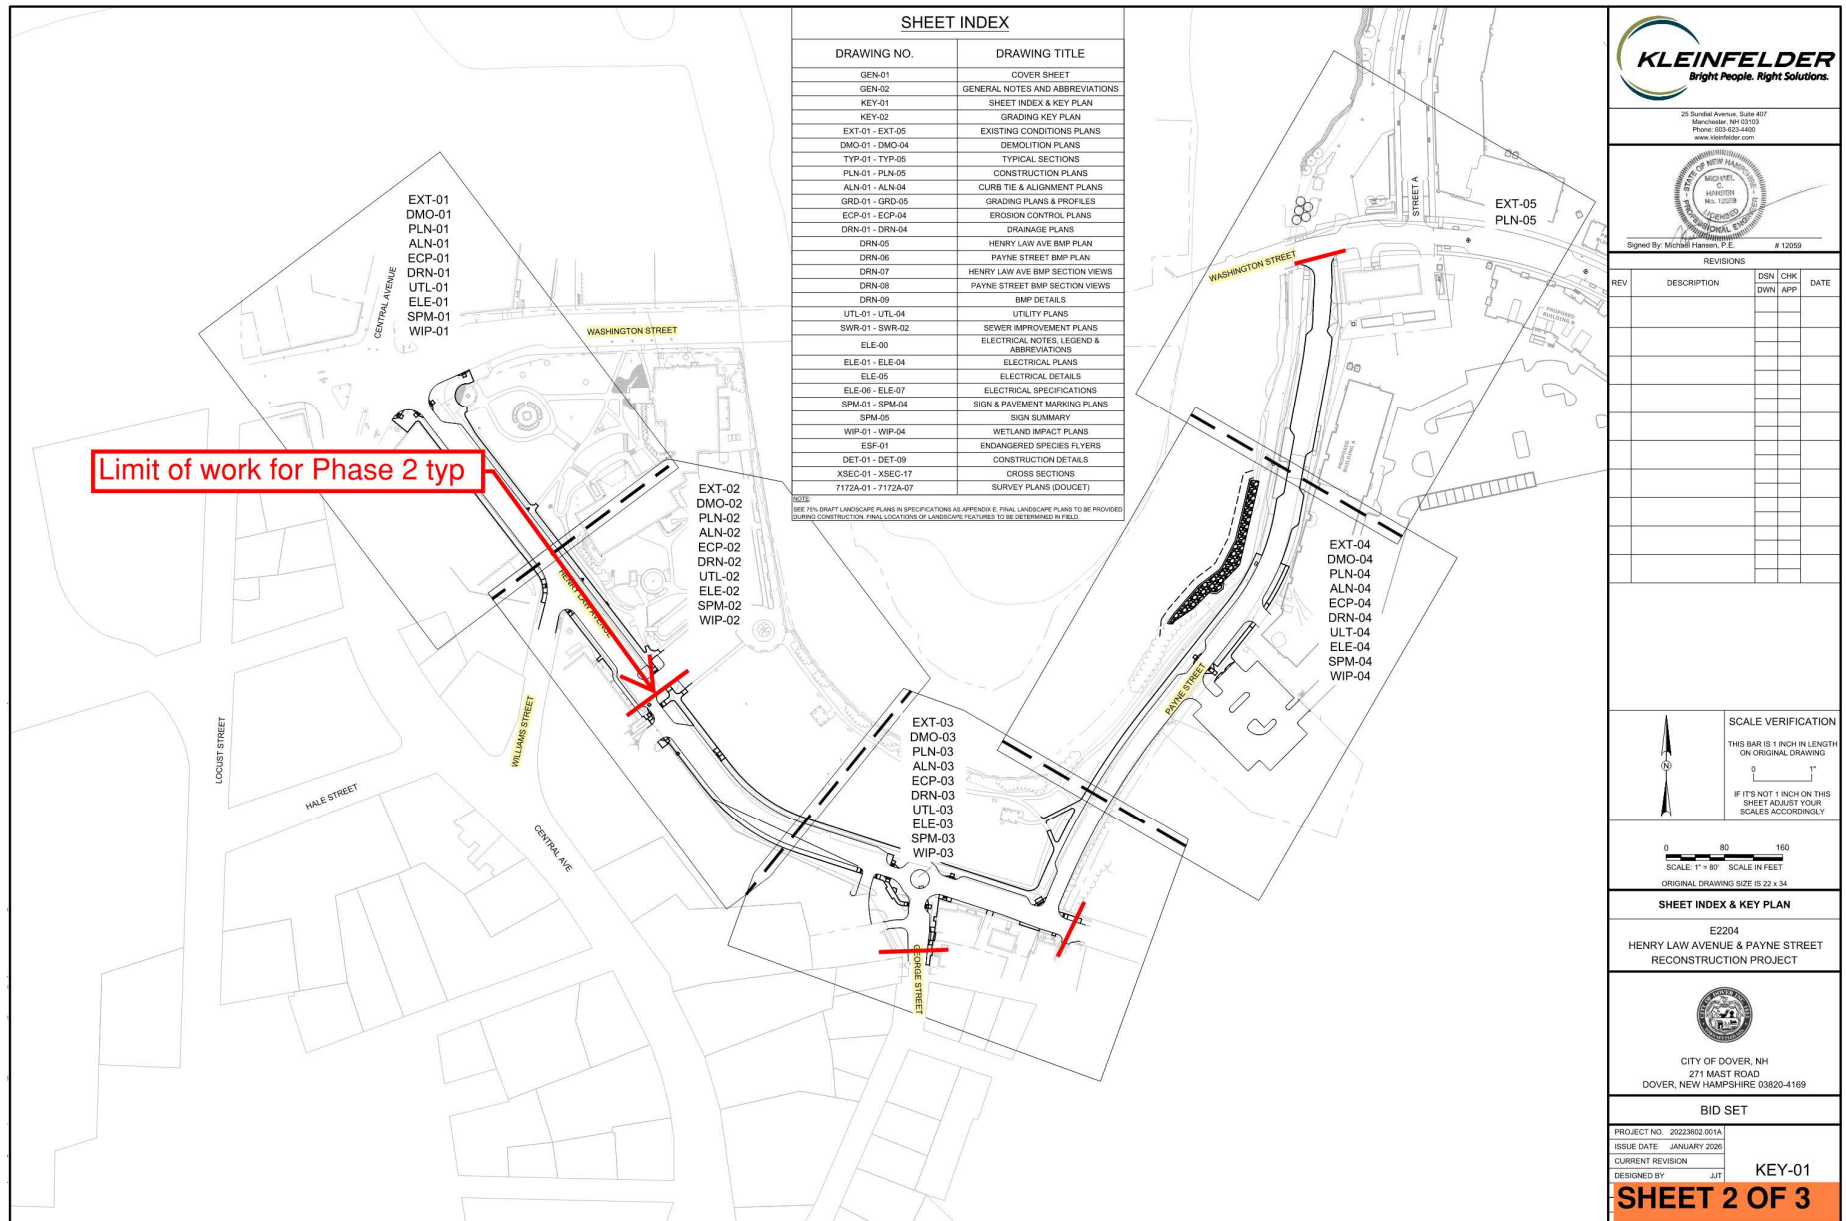

Phase 3

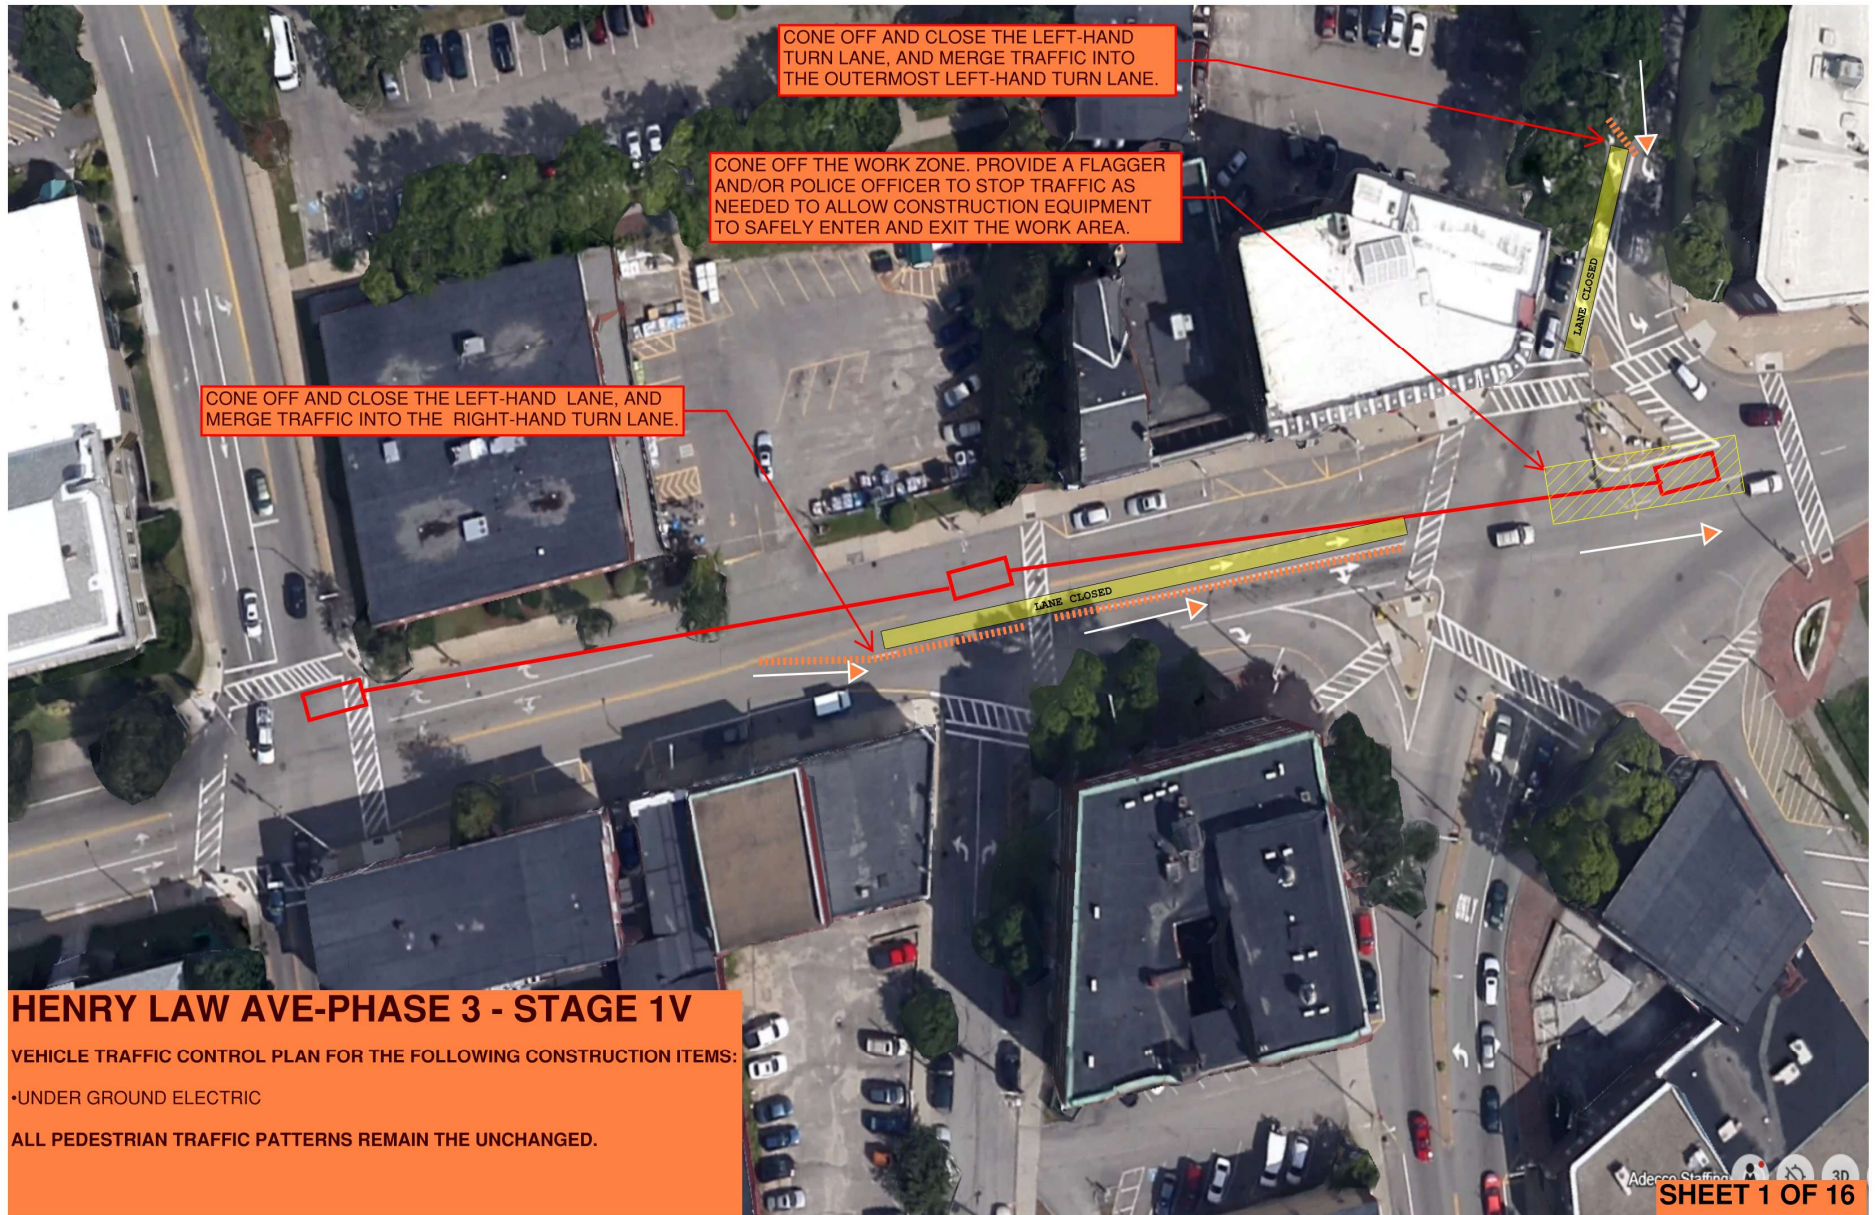



Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Work Complete	31, '26	Jun 7, '26
								M T W T F S	S M T W T F
1		TEST PITTING	10 days	Mon 7/20/26	Fri 7/31/26		0%		
2		PHASE 1 UTILITY WORK	80 days	Mon 8/3/26	Fri 11/20/26		0%		
3		Install Sewer Bypass	10 days	Mon 8/3/26	Fri 8/14/26		0%		
4		Sewer	30 days	Mon 8/17/26	Fri 9/25/26	3	0%		
5		Drainage	15 days	Mon 9/28/26	Fri 10/16/26	4	0%		
6		UGE	15 days	Mon 10/19/26	Fri 11/6/26	5	0%		
7		Site Lighting	10 days	Mon 11/9/26	Fri 11/20/26	6	0%		
8		PHASE 2 UTILITY WORK	227 days	Mon 11/23/26	Tue 10/5/27	7	0%		
9		Water	15 days	Mon 11/23/26	Fri 12/11/26		0%		
10		Drainage	70 days	Mon 12/14/26	Fri 3/19/27	9	0%		
11		CIPP	20 days	Mon 11/23/26	Fri 12/18/26	7	0%		
12		Bank Stabilization	65 days	Mon 12/21/26	Fri 3/19/27	11	0%		
13		UGE	50 days	Mon 3/22/27	Fri 5/28/27	12	0%		
14		Site Lighting	22 days	Mon 5/31/27	Tue 6/29/27	13	0%		
15		PHASE 1 STAGE 2 ROAD FINISH WORK	299 days	Wed 6/30/27	Mon 8/21/28		0%		
16		Box Roadway	10 days	Wed 6/30/27	Tue 7/13/27		0%		
17		Install Pavement Gravels	10 days	Wed 7/14/27	Tue 7/27/27	16	0%		
18		Fine Grade	1 day	Wed 7/28/27	Wed 7/28/27	17	0%		
19		Base Pave	1 day	Thu 7/29/27	Thu 7/29/27	18	0%		
20		Granite Curbing	2 days	Fri 7/30/27	Mon 8/2/27	19	0%		
21		Prep Concrete & Brick Sidewalks	5 days	Tue 8/3/27	Mon 8/9/27	20	0%		
22		Install Concrete Sidewalk	5 days	Tue 8/10/27	Mon 8/16/27	21	0%		
23		Install Brick Sidewalk	10 days	Tue 8/17/27	Mon 8/30/27	22	0%		
24		Raise Castings to Finish Grade	1 day	Tue 7/18/28	Tue 7/18/28		0%		
25		Finish Pave (Finish Paving to Follow Addendum #3 Work)	1 day	Thu 7/27/28	Thu 7/27/28	51	0%		
26		Install Pavement Marking (30 Days After Finish Paving)	1 day	Mon 8/21/28	Mon 8/21/28		0%		
27		Install Traffic Signs	1 day	Fri 7/28/28	Fri 7/28/28	53	0%		
28		PHASE 2 STAGE 2 ROAD AND PARK FINSH WORK	300 days	Tue 8/31/27	Mon 10/23/28		0%		
29		Box Roadway	22 days	Tue 8/31/27	Wed 9/29/27		0%		
30		Install Pavement Gravels	20 days	Thu 9/30/27	Wed 10/27/27	29	0%		
31		Fine grade	2 days	Thu 10/28/27	Fri 10/29/27	30	0%		
32		Base Pave	2 days	Mon 11/1/27	Tue 11/2/27	31	0%		
33		Granit Curbing	4 days	Wed 11/3/27	Mon 11/8/27	32	0%		
34		Prep Concrete & Brick Sidewalks	10 days	Tue 11/9/27	Mon 11/22/27	33	0%		
35		Install Concrete Sidewalk	10 days	Tue 11/23/27	Mon 12/6/27	34	0%		
36		Install Brick Sidewalk	5 days	Tue 12/7/27	Mon 12/13/27	35	0%		
37		Electrical Work (Panel Install, Pulling Wire and Miscellaneous Items)	60 days	Mon 3/13/28	Fri 6/2/28		0%		
38		Tree Protection	1 day	Mon 6/5/28	Mon 6/5/28	37	0%		

Project: Henry Law Ave Phase S
Date: Tue 7/14/26

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Work Complete	31, '26	Jun 7, '26
								M T W T F S	S M T W T F
39		Concrete Base for Art Work	1 day	Tue 6/6/28	Tue 6/6/28	38	0%		
40		Flag Pole	2 days	Wed 6/7/28	Thu 6/8/28	39	0%		
41		Loam	30 days	Fri 6/9/28	Thu 7/20/28	40	0%		
42		Trees	10 days	Fri 7/21/28	Thu 8/3/28	41	0%		
43		Shrubs	10 days	Fri 8/4/28	Thu 8/17/28	42	0%		
44		Fence	2 days	Fri 8/18/28	Mon 8/21/28	43	0%		
45		Turf	5 days	Tue 8/22/28	Mon 8/28/28	44	0%		
46		Seeding	2 days	Tue 8/29/28	Wed 8/30/28	45	0%		
47		Benches	5 days	Thu 8/31/28	Wed 9/6/28	46	0%		
48		Bollards	3 days	Thu 9/7/28	Mon 9/11/28	47	0%		
49		Final Park Cleanup and Punch List Items	30 days	Tue 9/12/28	Mon 10/23/28	48	0%		
50		Raise Castings to Finish Grade	15 days	Tue 7/4/28	Mon 7/24/28	54	0%		
51		Finish Pave (Finish Paving to Follow Addendum #3 Work)	2 days	Tue 7/25/28	Wed 7/26/28	50	0%		
52		Install Pavement Marking (30 Days After Finish Paving)	2 days	Fri 8/25/28	Mon 8/28/28		0%		
53		Install Traffic Signs	1 day	Thu 7/27/28	Thu 7/27/28	51	0%		
54		Addendum #3 Electrical Duct Bank from Henry Law Ave to Chestnut Street	36 days	Mon 5/15/28	Mon 7/3/28		0%		
55		Test Pitting	5 days	Mon 5/15/28	Fri 5/19/28		0%		
56		Install Electrical Duct Bank (Approx 550-lf)	20 days	Mon 5/22/28	Fri 6/16/28	55	0%		
57		Install Electrical Manholes (Qty 3)	6 days	Mon 6/19/28	Mon 6/26/28	56	0%		
58		Pavement Prep and Pave	5 days	Tue 6/27/28	Mon 7/3/28	57	0%		
59							0%		

Project: Henry Law Ave Phase S
Date: Tue 7/14/26

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Questions?
